

HIGHLAND SPRING GROUP

BLACKFORD FREIGHT FACILITY

COMMUNITY PROGRESS UPDATE

11/03/22

Please find below a summary of the works recently undertaken at the Blackford Freight Facility and a two-week lookahead programme.

Summary of Works Undertaken:

- Set-up our site compound and traffic management system.
- Took delivery of sleepers and rails.
- Took delivery ballast for installing in week commencing 14/03/22.
- Commenced installation of sleepers and rails for both sidings.
- Commenced track welding with 36 of 82 total welds now complete.

Two-Week Lookahead (14/03/22 - 28/03/22):

- Complete all remaining track welding.
- Take delivery of and install remaining ballast throughout both sidings.

Traffic management system throughout the village will continue to be monitored by the site team and we will continue to liaise with our material suppliers about conformance with the Traffic Management Plan.

If you have any questions or queries about our work in Blackford, please call or email Highland Spring Group on **01764 660637** or email blackfordrail@highlandspringgroup.com
All site operatives have been advised to direct queries to this phone number.

Progress Photos





Figures 1-4 – Newly Installed Signage




Figures 5-8 – Site Compound Established within Freight Facility



Figures 9-11 – Traffic Management System Established

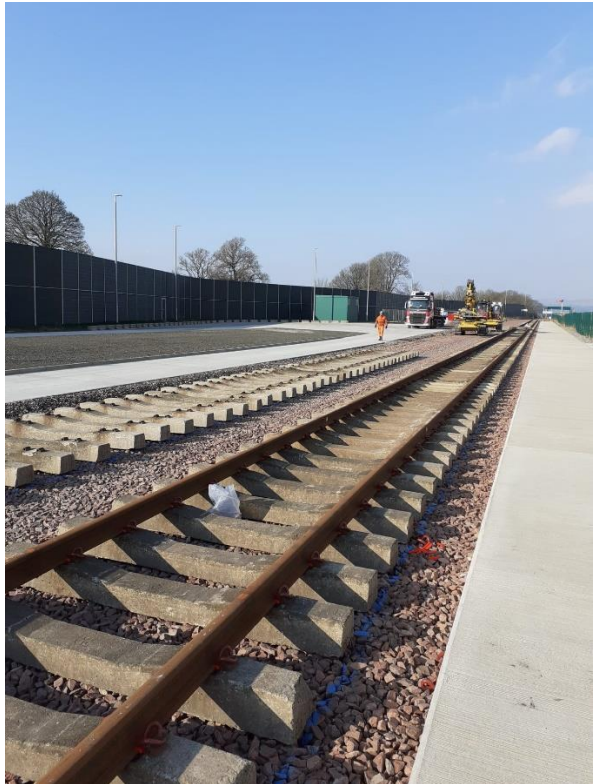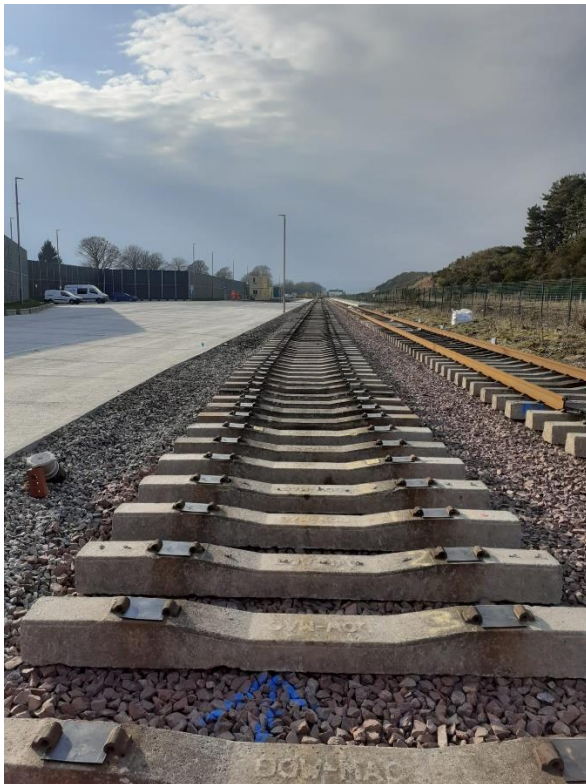

Figures 12-14 – Installation of sleepers and rails for sidings No. 1 & No. 2

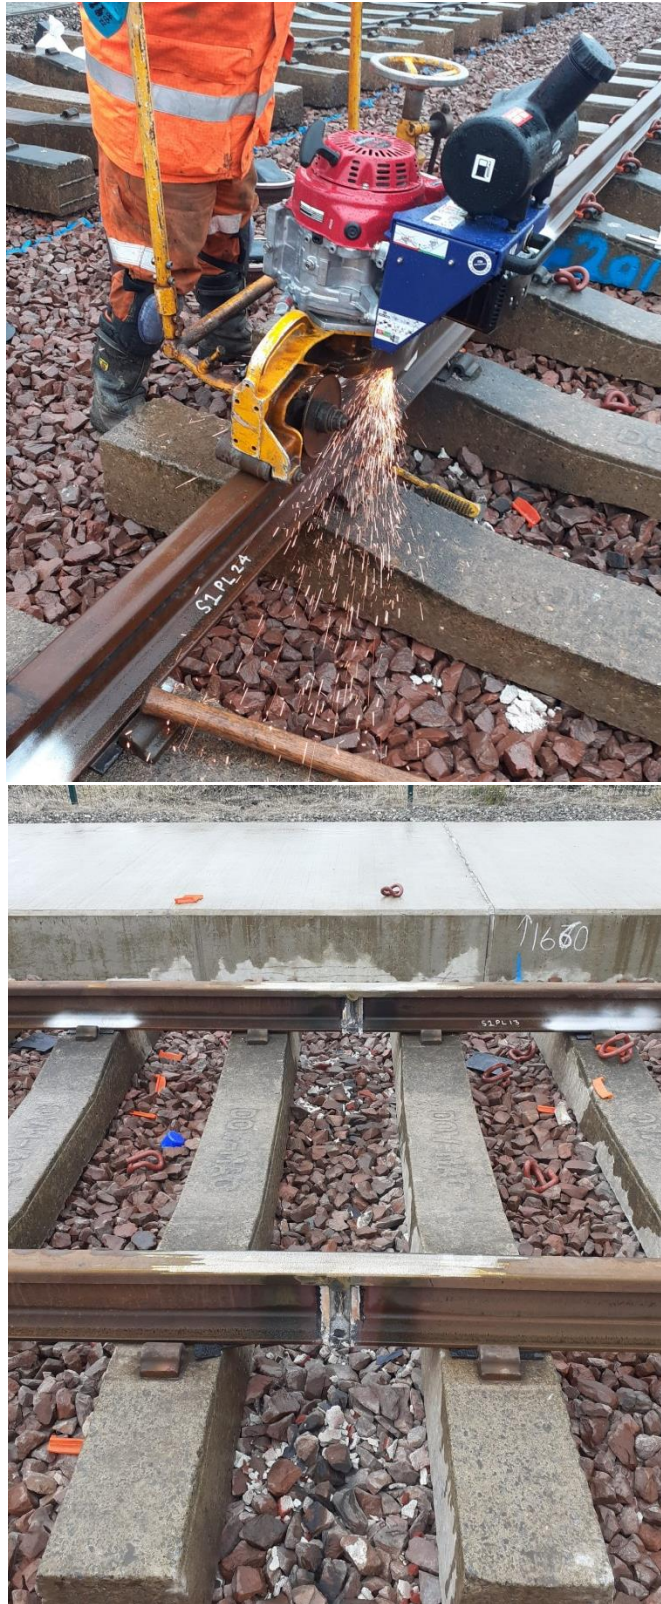

Figures 15-16 – Track Welding



Figures 17-18 – Ariel Views of the Freight Facility
